

I-35 at FM 3406

Project Overview: The intersection of FM 3406 and the I-35 frontage roads are being improved, and the FM 3406 bridge over I-35 is being reconstructed.

Length: .42 miles


Construction cost: \$12.4 million

Construction start: March 2017

Estimated completion: Late 2018, weather permitting

Project Update:

- **Upcoming work:** Continuing with drainage work and placing sidewalk. South and northbound frontage road driveway work.
- **Work completed:** FM 3406 bridge completed, detour traffic control removed, and retaining wall work implemented. Eastbound FM 3406 median work. Traffic switch onto new south and northbound frontage roads. Opened north to southbound U-turn bridge.

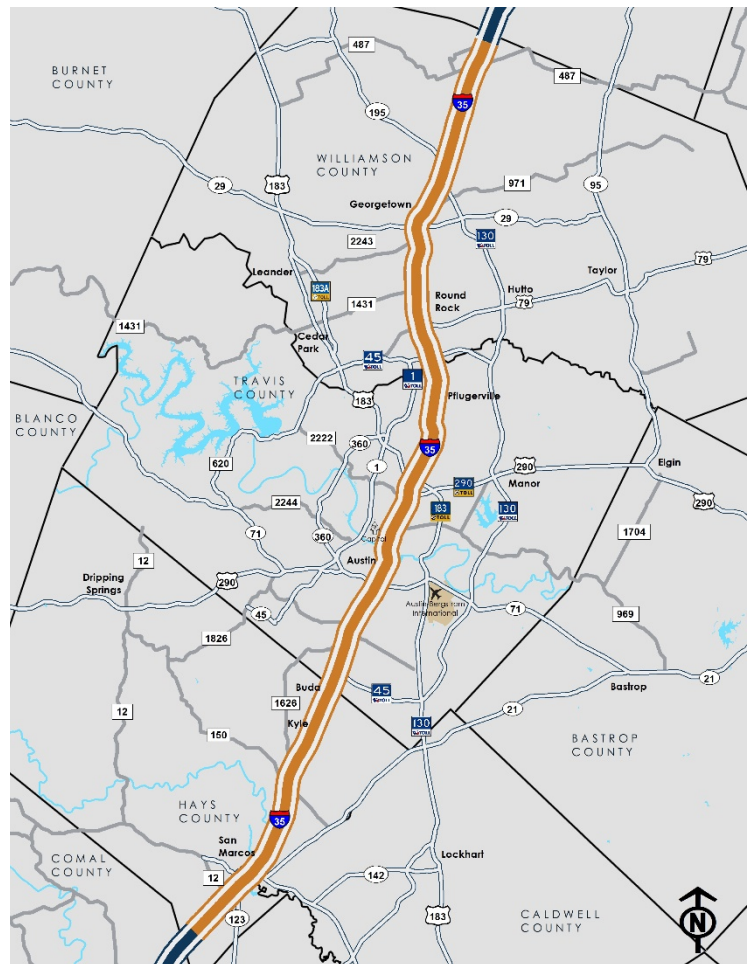



Place Topsoil for Seeding at Rudy's and Mellow Mushroom



Pave Chuys and Cracker Barrel Driveway




Complete Denny's Driveway, Share Used Path and Ramps



Pour and Finish Toyota/Honda Driveway



Pave Wolle Lane



Pave McDonald's and Chevron Driveway
