

I-35 at FM 3406

Project Overview: The intersection of FM 3406 and the I-35 frontage roads are being improved, and the FM 3406 bridge over I-35 is being reconstructed.

Length: .42 miles


Construction cost: \$12.4 million

Construction start: March 2017

Estimated completion: Early 2019, weather permitting

Project Update:

- **Upcoming work:** Northbound frontage road work and final configuration. Complete project.
- **Work completed:** FM 3406 bridge completed, detour traffic control removed, and retaining wall work implemented. Eastbound FM 3406 median work. Traffic switch onto new south and northbound frontage roads. Opened north and southbound U-turn bridges. Driveway work complete. Drainage and bicycle and pedestrian paths complete. Southbound frontage road complete.

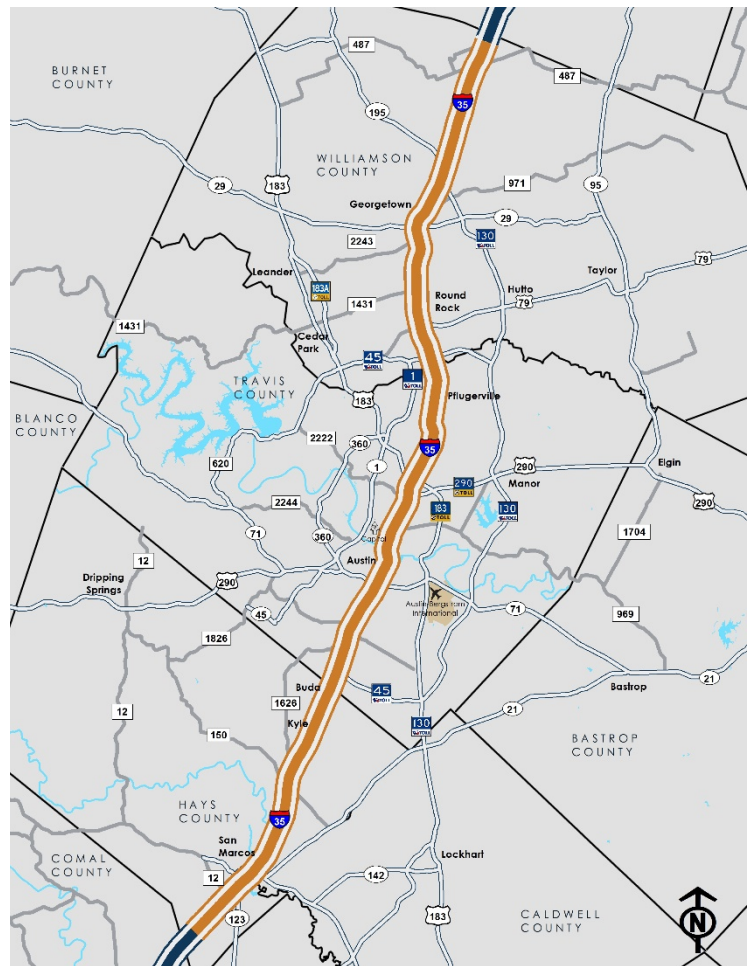



Pave last section of the northbound frontage road



Pave last section of northbound frontage road



Attend Ribbon Cutting Ceremony with TxDOT and Elected Officials



Cut the Ribbon!



Complete paver work in center island



Walk jobsite with owner for punch list
