

I-35 at FM 3406

Project Overview: The intersection of FM 3406 and the I-35 frontage roads are being improved, and the FM 3406 bridge over I-35 is being reconstructed.

Length: .42 miles


Construction cost: \$12.4 million

Construction start: March 2017

Estimated completion: Early 2019, weather permitting

Project Update:

- **Upcoming work:** Northbound frontage road work and final configuration. Complete project.
- **Work completed:** FM 3406 bridge completed, detour traffic control removed, and retaining wall work implemented. Eastbound FM 3406 median work. Traffic switch onto new south and northbound frontage roads. Opened north and southbound U-turn bridges. Driveway work complete. Drainage and bicycle and pedestrian paths complete. Southbound frontage road complete.

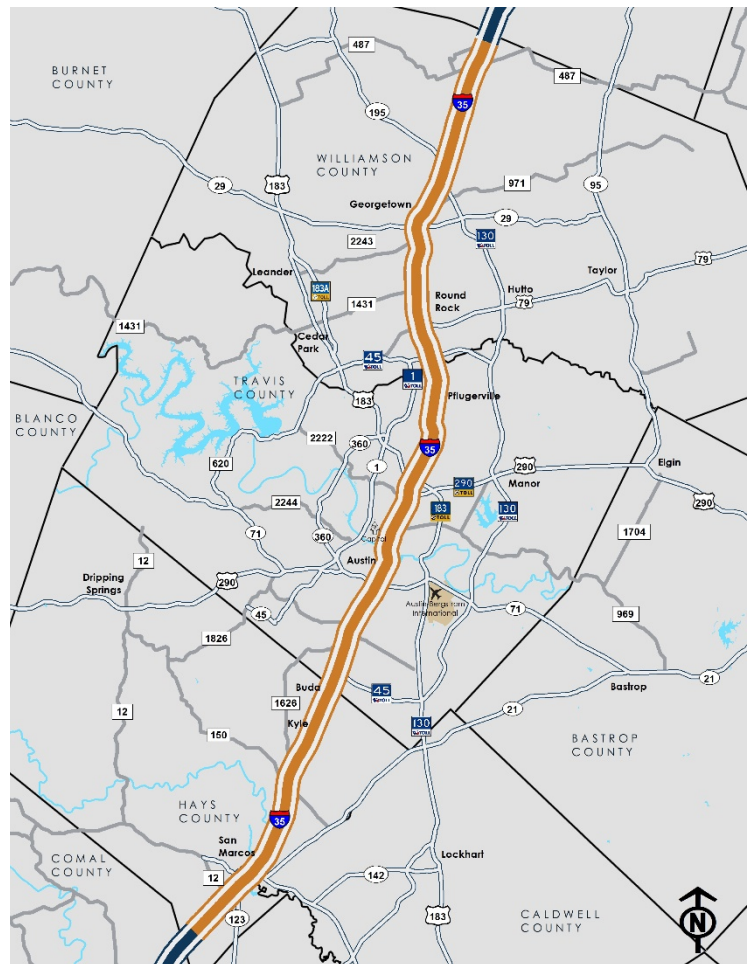




Perform emergency repair of I-35 mainlane barrier



Pour and finish shared used path at Toyota



Finish landscape pavers at Toyota

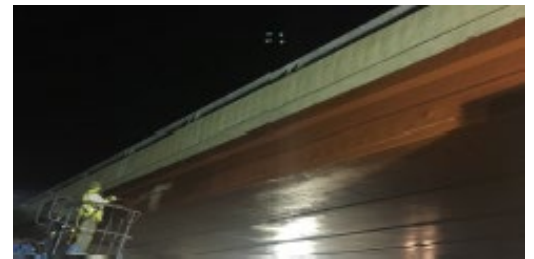

Paint bridge girders per aesthetic detail



Prep flexbase for final asphalt paving



Dewater job-site and recover grade
