

**I-35 at FM 3406**

**Project Overview:** The intersection of FM 3406 and the I-35 frontage roads are being improved, and the FM 3406 bridge over I-35 is being reconstructed.

**Length:** .42 miles


**Construction cost:** \$12.4 million

**Construction start:** March 2017

**Estimated completion:** Late 2018, weather permitting

**Project Update:**

- **Upcoming work:** Continuing with drainage work and placing sidewalk. South and northbound frontage road driveway work.
- **Work completed:** FM 3406 bridge completed, detour traffic control removed, and retaining wall work implemented. Eastbound FM 3406 median work. Traffic switch onto new south and northbound frontage roads. Opened north to southbound U-turn bridge.

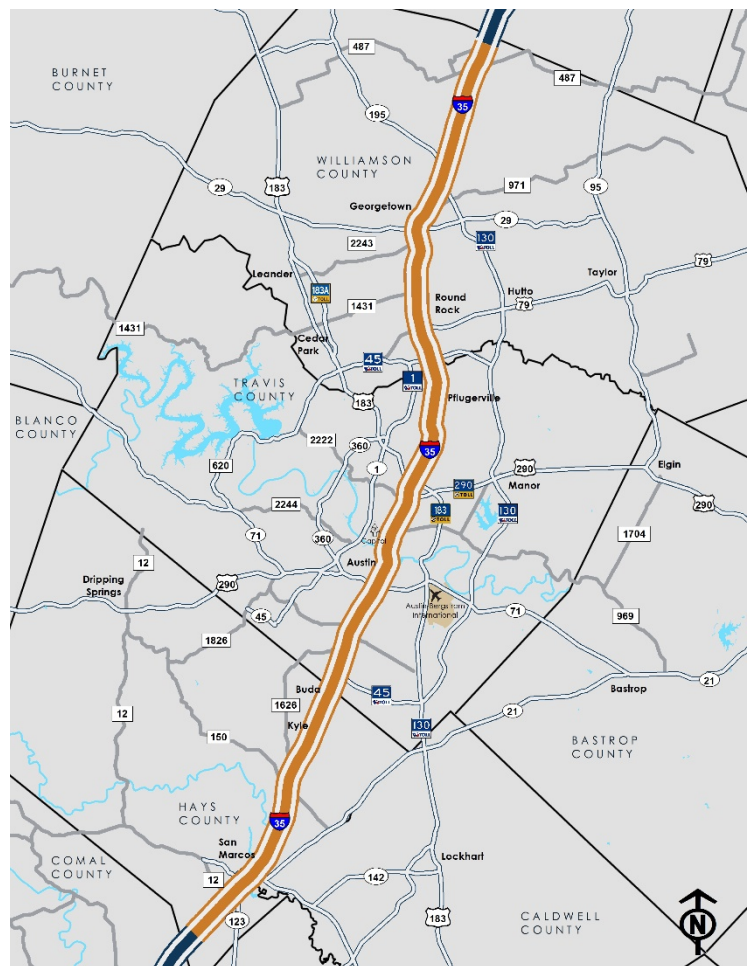



FCI: Pour Pedestrian Rail and Backfill Wall



AARON Concrete: Place Curb and Gutter



FCI: Dewatering/Dressing slopes/SWPPP



FCI: Discuss Vehicle Damage Policy at Toolbos Talk



AARON: Place Shared Used Path



FCI: Storm Sewer Work Along Frontage Roads
